

Sprint 2 – Sprint Planning Meeting Summary

Date: 15 April 2026

Type: Sprint Planning Meeting

Duration: ~27 minutes (WhatsApp Call)

Attendees

All team members present

Sprint Goal

To implement core Sprint 2 features including cart functionality, order management, database logic, and real-time updates, while improving task structure and team collaboration from Sprint 1.

Sprint Backlog Selection

The team reviewed the full list of required features for Sprint 2 and selected the following focus areas:

- Cart and order placement
- Database and backend logic
- Vendor dashboard and order management
- Order status updates
- Student tracking interface
- Real-time updates and notifications

These features were broken down into structured **user stories**, each supported by **acceptance tests** and **implementation tasks**.

Task Breakdown Approach

The team agreed that:

- User stories must follow the **Who–What–Why format**
- Acceptance tests must follow **Given–When–Then structure**
- Tasks must:
 - Be small and manageable
 - Directly support the user story
 - Represent actual implementation steps

It was emphasised that:

- User stories represent **features**, not small tasks
 - Code must align with both the **user story and its tasks**
-

Task Allocation Strategy

- Tasks were grouped based on **functional components** and **system dependencies**
- Each team member selected tasks aligned with their role
- Responsibilities were clearly assigned to ensure:
 - Balanced workload
 - Individual accountability
 - Improved ownership compared to Sprint 1

The team agreed that:

- Members are responsible for their own tasks
 - Work should not be completed on behalf of others
 - Collaboration should focus on discussion, not duplication
-

Sprint 1 Retrospective Insights Applied

The team identified key issues from Sprint 1:

- Uneven workload distribution
- Lack of clear ownership
- Inconsistent contribution levels

To address this, the team committed to:

- Better task breakdown and clarity
 - Equal participation across members
 - Stronger communication and accountability
-

Workflow Agreements

Project Board (GitHub Projects)

The team agreed to use the board as follows:

- **Backlog** → All identified work
- **Ready** → Approved items for development
- **In Progress** → Active work
- **Done** → Completed and reviewed work

Team members must:

- Keep the board updated
 - Move tasks as progress is made
 - Use the board to track contributions
-

Git Workflow

- Each member works on their **own branch**
- No direct commits to the main branch
- All work must be submitted via **pull requests**

Code Review Process:

- **Sthembile** assigned as main reviewer
- Responsible for reviewing all pull requests
- Only approved code is merged into main

This ensures:

- Code quality
 - Consistency
 - Accountability
-

Technical Decision

Authentication System Update:

- Removed: Forgot Password functionality
- Added: OTP (One-Time Password) system

Reasoning:

- More secure approach
 - Simpler user flow
 - Improved user experience
-



Definition of Done (Agreed Implicitly)

A task is considered complete when:

- It satisfies the user story requirements
 - Acceptance tests are met
 - Code is pushed via pull request
 - Code is reviewed and approved
 - Task is moved to **Done** on the board
-

Summary

This meeting established the structure and direction for Sprint 2. The team clearly defined how work will be broken down, assigned, and managed, while addressing shortcomings from Sprint 1. Tasks were distributed evenly, workflows were formalised, and a shared understanding of responsibilities was achieved before development began.

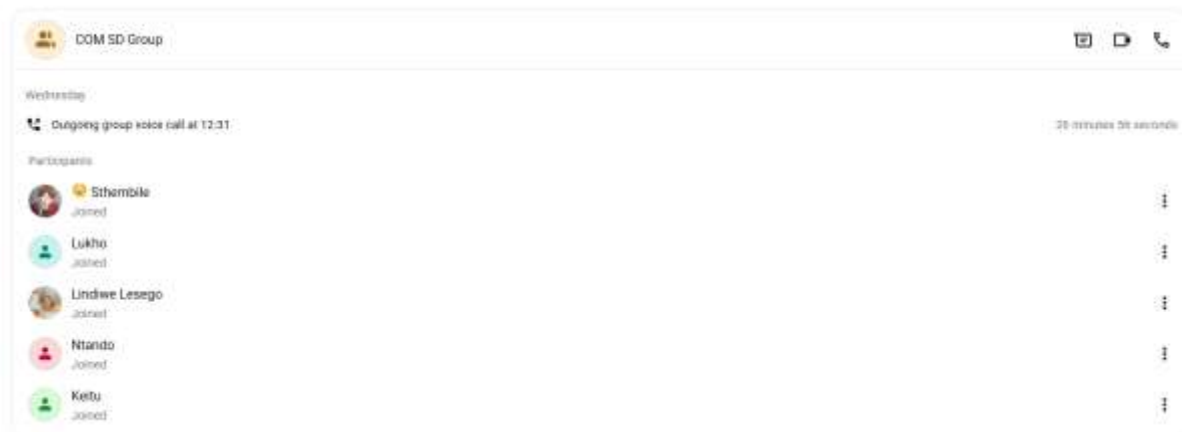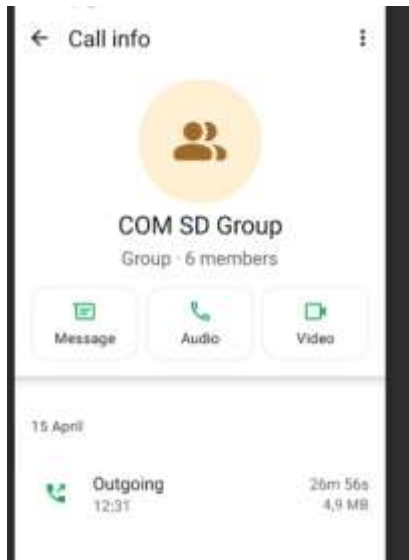

Sprint 2 Daily Scrum Summary

Date: 17 April 2026

Type: Daily Scrum (Stand-up)

Duration: ~16 minutes (WhatsApp Call)

Attendees

All team members present

Purpose of Meeting

To provide quick progress updates, check alignment, and ensure continued progress toward Sprint 2 goals.

Individual Progress Updates

Each team member briefly reported on:

- What they have completed so far
 - What they are currently working on
 - What they plan to complete next
-

Discussion Points

- Team members confirmed steady progress across all assigned tasks
 - No major blockers or issues were raised
 - Work remains aligned with Sprint 2 user stories and task allocations
 - Reminder given to maintain consistent progress and meet deadlines
-

Process Reminders

- All completed work must be:
 - Pushed to individual branches
 - Submitted via pull requests
- **Sthembile (Code Reviewer):**

- Responsible for reviewing all pull requests
- Only approved work will be merged into the main branch

Blockers / Issues


- No blockers or challenges were reported during this meeting


Next Steps

- Continue working on assigned tasks
- Submit completed work for review
- Maintain regular updates on the project board
- Ensure all contributions go through the correct Git workflow

Summary

This was a short alignment meeting to ensure all team members are progressing as expected. Work is on track, with no issues identified, and all members are continuing with their assigned responsibilities.

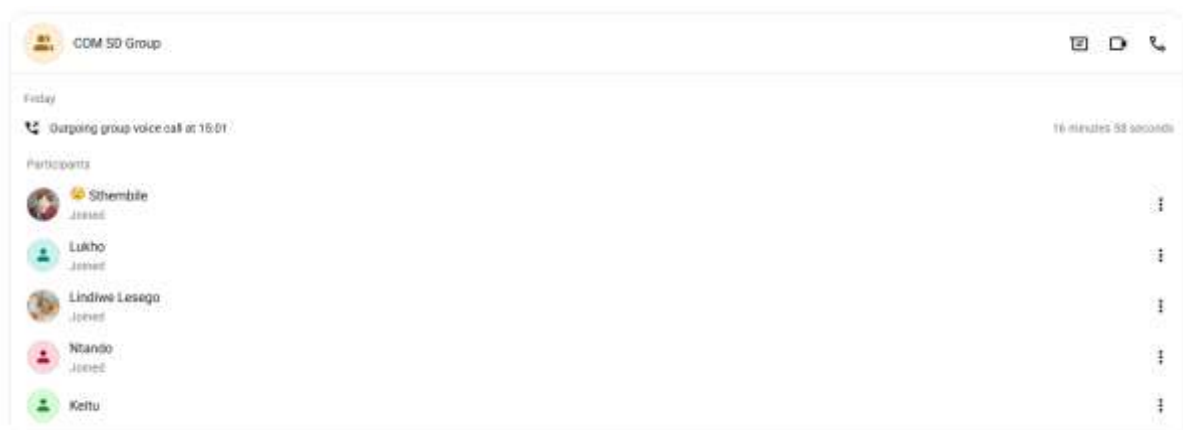

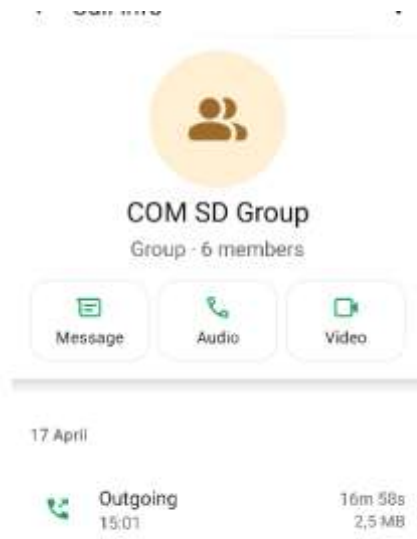

Sprint 2 Daily Scrum Summary

Date: 19 April 2026

Type: Daily Scrum (Stand-up)

Duration: ~29 minutes (WhatsApp Call)

Attendees

All team members present

Purpose of Meeting

To review overall project progress, confirm completion of Sprint 2 tasks, and identify any remaining work before final submission.

Progress Overview

- The team confirmed that **all major features and tasks have been completed**
- The system flow was reviewed end-to-end to ensure proper integration between components
- All implemented functionality aligns with the defined user stories and acceptance tests

Discussion Points

- The team walked through **how all parts of the system connect and function together**
- Confirmed that **Sprint 2 implementation is nearly complete**
- Identified **remaining minor issues to be addressed:**

- Completion of the **notifications feature**
- Fix required to ensure students can view:
 - Time the order was placed
 - Time the order status changed (e.g., received/ready)

Blockers / Issues


- No major blockers were reported
- Only minor functionality fixes and final feature completion remain

Next Steps

- Finalise the **notifications functionality**
- Fix and verify **order timestamp display for students**
- Perform final testing to ensure all features work correctly
- Prepare the system for final submission and demonstration

Summary

This meeting confirmed that the project is **functionally complete**, with all major Sprint 2 tasks implemented. The team ensured that the full system flow is working correctly and identified only minor remaining tasks. The project is now in the **final refinement and testing stage**, with completion imminent.

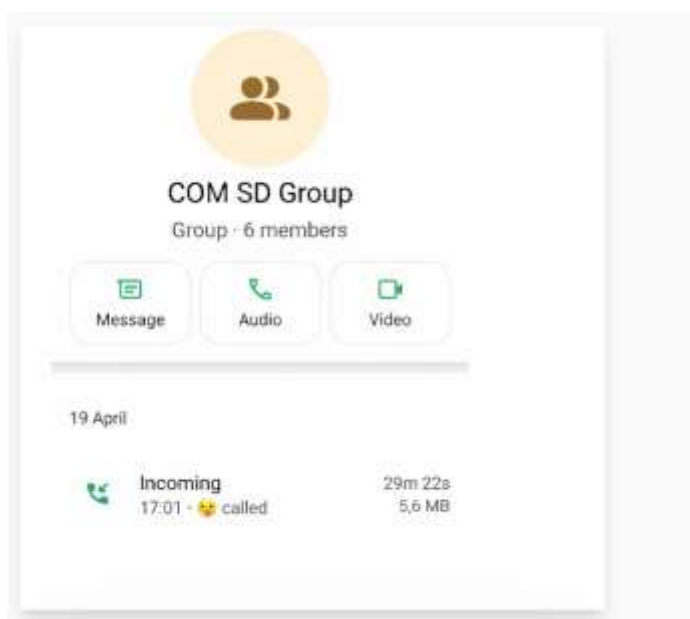

Sprint Retrospective Meeting Summary

Date: 20 April 2026

Duration: 10 minutes

Platform: WhatsApp Call

Attendees: All team members

1. What Went Well

The team demonstrated strong performance throughout the sprint, particularly in task management and collaboration.

- Task distribution improved significantly, ensuring that each member had a fair and meaningful contribution.
- Communication was effective, with regular WhatsApp meetings that were efficient and sufficient.
- The team followed a structured Git workflow:
 - Each member worked on their own feature branch.
 - A designated member handled merges to the main branch.
- The CI/CD pipeline functioned smoothly without issues.
- All tasks were completed on time.

Key Highlights:

- Clear and balanced task allocation across the team.
 - Effective use of Git branches and pull requests.
 - Strong collaboration and consistent communication.
-

2. What Didn't Go Well

While most aspects of the sprint were successful, there was one key oversight:

- The **software architecture (UML diagrams)** was left too late and only completed at the last minute.
- This occurred because the requirement was not identified early enough.

Notably:

- No missed deadlines, major bugs, or workload imbalance.

- Core development tasks were completed successfully.
-

3. Challenges / Blockers

The team experienced minimal blockers during this sprint.

- Work dependencies were handled well, with foundational components completed early.
- This allowed dependent tasks to proceed without delay.

Primary Challenge:

- The **one-week sprint duration was quite short**, increasing pressure on completing all deliverables.
-

4. What Can Be Improved

The team agreed to maintain the current workflow, as it was effective, while making small refinements:

- Ensure that **all deliverables (including UML and documentation)** are identified and started earlier in the sprint.
- Continue prioritizing critical and dependency-heavy tasks early.

Key Improvement Strategy (to continue):

- Starting difficult or dependency-based features early worked very well this sprint.
- Team members responsible for code that others depended on completed their work immediately, allowing the rest of the team sufficient time to complete their tasks.
- Tasks were allocated strategically:
 - Members with stronger time management, more experience, or immediate availability handled high-priority and foundational components first.
- This prioritisation improved overall efficiency and reduced delays.

The team will **continue using this same task allocation and prioritisation strategy in future sprints**.

5. Action Items for Next Sprint

- Begin **non-coding deliverables (e.g., UML diagrams)** earlier.
 - Maintain the current Git workflow (feature branches + designated merge member).
 - Continue prioritising and completing dependency-heavy tasks early.
 - For longer sprints (e.g., 3 weeks), hold **2–3 meetings per week**.
-

6. Team Collaboration Reflection


- All members contributed actively and equally.
 - Communication was consistent and responsive.
 - Full attendance in meetings.
 - Strong teamwork with no major issues.
-

7. Tools & Workflow Review

- **GitHub Projects board** was effective for tracking progress.
 - **CI/CD pipeline** worked smoothly.
 - **Codecov** was slightly confusing for some members and may require clarification.
-

Overall Summary

This sprint was highly successful, with strong collaboration, efficient task execution, and effective communication. The main improvement area is ensuring that all deliverables, including UML diagrams, are addressed earlier. The team will continue using its successful task prioritisation and workflow strategy moving forward.





COM SD Group

Group · 6 members



20 April



Outgoing
10:00

11m 32s
2,4 MB
