

Sprint 4 — Scrum Meeting 1

Sprint Planning and Task Breakdown Meeting

Date: 12 May 2026

Duration: 25 minutes

Meeting Type: Sprint 4 Planning / First Scrum Meeting

Sprint Goal: Build an **Analytics section** for the Campus Food Ordering Platform.

The team met to discuss and break down the work required for Sprint 4. The main goal for this sprint is to create an admin analytics section that allows the system to display useful sales and order information. The analytics section will include sales per vendor over time, peak ordering hours, a custom filtered analytics view, and the ability to export reports as CSV or PDF.

Main Sprint 4 Goal

The Sprint 4 goal is to build an **Analytics section** with the following features:

1. Sales per vendor over time
 2. Peak ordering hours
 3. Custom analytics view
 4. Export reports as CSV or PDF
-

Task Breakdown and Team Roles

Person	Role	Main Feature
Person 1	Analytics Backend Developer	Prepare analytics data/API
Person 2	Analytics Dashboard UI Developer	Create dashboard page and layout
Person 3	Sales Report Developer	Sales per vendor over time
Person 4	Time Report Developer	Peak ordering hours
Person 5	Custom Report Developer	Custom filtered analytics view
Person 6	Export Feature Developer	Export reports as CSV/PDF

Work Order and Dependencies

The team agreed on the following work order:

Step 1: Person 1 starts first

Person 1 will prepare the analytics backend/data foundation. This is the first task because all other reports depend on clean and correct analytics data.

Step 2: Person 2 starts the dashboard layout

Person 2 can begin early using mock/sample data. Once Person 1 finishes the real analytics data format, Person 2 will connect the dashboard to the real data.

Step 3: Persons 3, 4, and 5 build the reports

Once Person 1 confirms the data format, Persons 3, 4, and 5 can work at the same time.

- Person 3 builds the sales per vendor report.
- Person 4 builds the peak ordering hours report.
- Person 5 builds the custom analytics view.

Step 4: Person 6 builds export functionality

Person 6 starts once the report data structures are clear. Their export feature depends on the reports created by Persons 3, 4, and 5.

Step 5: Everyone tests their own feature

Each person is responsible for testing their own part before merging.

Individual Responsibilities

Person 1 — Analytics Backend / Data Foundation

Main Tasks:

- Identify the required database tables.
- Fetch only valid paid orders.
- Calculate order totals.
- Return vendor name, order date, order time, order total, and order status.
- Create reusable helper functions for analytics.
- Give the team the final data format.

Depends on:

Person 1 starts first and does not depend on anyone else.

People depending on Person 1:

Persons 2, 3, 4, 5, and 6.

Person 2 — Analytics Dashboard Page / Layout**Main Tasks:**

- Create the main analytics page.
- Add dashboard heading and navigation.
- Add sections/cards for each report.
- Create consistent styling for tables, buttons, filters, and report cards.
- Add loading, error, and empty-state areas.
- Connect the page to Person 1's analytics data once ready.

Depends on:

Can start with mock data, but needs Person 1's real data later.

People depending on Person 2:

Persons 3, 4, 5, and 6 need the dashboard space for their reports.

Person 3 — Sales Per Vendor Over Time Report**Main Tasks:**

- Use Person 1's analytics data.
- Group orders by vendor.
- Group sales by date.
- Calculate total sales per vendor.
- Show number of orders per vendor.
- Display the report in a table or chart.
- Add a date range filter if possible.

Depends on:

Person 1 for clean analytics data and Person 2 for the dashboard section.

Person 4 — Peak Ordering Hours Report

Main Tasks:

- Use Person 1's analytics data.
- Extract the hour from each order time.
- Count orders per hour.
- Sort from busiest hour to quietest hour.
- Display the result in a table or chart.
- Highlight the busiest ordering hour.

Depends on:

Person 1 for order time data and Person 2 for the dashboard section.

Person 5 — Custom Analytics View

Main Tasks:

- Build the custom analytics section.
- Add filters for vendor, start date, end date, order status, and payment status.
- Apply filters to the analytics data.
- Show filtered results in a table.
- Make sure the filtered data can be exported by Person 6.

Depends on:

Person 1 for clean data and Person 2 for the dashboard section.

People depending on Person 5:

Person 6 depends on Person 5 because filtered data must export correctly.

Person 6 — Export Reports as CSV/PDF

Main Tasks:

- Create reusable export buttons.
- Add export buttons to the sales report, peak ordering hours report, and custom analytics view.
- Create a CSV export function.
- Create a PDF export function.
- Make sure exported files have proper names.
- Make sure filtered reports export only filtered data.
- Work with Persons 3, 4, and 5 to receive their final report data.

Depends on:

Persons 3, 4, and 5 because their report data must exist before exporting. Also depends on Person 2 because the export buttons must fit neatly into the dashboard layout.

Meeting Outcome

By the end of the meeting, the team had agreed on the Sprint 4 goal, the main analytics features, the individual roles, and the correct order of work. The team also identified the key dependencies between members to avoid confusion during implementation. Person 1 must begin first with the analytics data foundation, while Person 2 can begin the dashboard layout using mock data. Once the data format is confirmed, Persons 3, 4, and 5 can build their reports, and Person 6 can complete the export functionality once the reports are ready.

Next Steps

The team will begin work according to the agreed dependency order. Person 1 will start with the analytics backend/data foundation and share the final data format with the rest of the team. Person 2 will begin preparing the dashboard layout. The rest of the team will prepare their report sections and begin implementation once the required data and dashboard structure are available.

← Call info



COM SD Group

Group · 6 members



Message



Audio



Video

12 May



Outgoing
17:00

25m 17s
3.8MB

Sprint 4 — Daily Scrum Meeting 1

Branch Coordination and Analytics Integration Meeting

Date: 15 May 2026

Duration: 13 minutes

Meeting Type: Daily Scrum Meeting

Sprint: Sprint 4 — Analytics

Main Focus: Person 1's completed analytics backend work and team coordination on the shared branch.

Meeting Summary

On 15 May, the team held a 13-minute daily scrum meeting to discuss the current progress of Sprint 4. During the meeting, Person 1 confirmed that their part of the Sprint 4 work had been completed. This included preparing the analytics data source and creating the GET /api/analytics endpoint, which provides clean paid-order data for the rest of the analytics reports. The endpoint returns useful fields such as vendor name, order date, order time, order hour, order total, payment status, and items.

The team also discussed how the remaining members should connect their work to Person 1's completed backend data. Since the rest of the Sprint 4 features depend on clean analytics data, this was an important point of discussion.

What Was Discussed

1. Person 1 Completed Their Work

Person 1 completed the analytics backend/data foundation. Their work allows the rest of the team to fetch and use clean analytics data from the API.

This means that Persons 2, 3, 4, 5, and 6 can now begin connecting their features to the real analytics data instead of only using mock data.

2. Connecting to Person 1's Analytics Data

The team discussed how each report should use the analytics data from:

GET /api/analytics

This data will be used by the dashboard, sales report, peak ordering hours report, custom analytics view, and export feature.

3. Branch Complications

The team discussed complications caused by everyone working on the same branch. The main concern was that if multiple people edit the same files, especially analytics.html, merge conflicts could happen.

The team agreed that everyone should always pull the latest updated version of the branch before continuing their own work. This helps make sure that everyone is working on the most recent code.

4. Final Branch Decision

The team decided to continue working on the same branch as Person 2.

This decision was made because Person 2 is responsible for the main analytics dashboard layout, and everyone else's work connects into that dashboard. The documents also state that Person 2 controls the main HTML layout, while Persons 3, 4, 5, and 6 should mainly work in their own JavaScript files to avoid overwriting each other's work.

Important Team Rule Agreed On

Everyone agreed to follow this rule:

Before making changes or pushing code, each person must first pull the latest version of the branch.

This means the team should regularly use:

git checkout feature/analytics-dashboard-UI

git pull origin feature/analytics-dashboard-UI

This will help prevent people from working on old code.

Branch Conflict Prevention Plan

Rule	Reason
Everyone works on the same branch as Person 2	Keeps the analytics dashboard work together
Everyone must pull before editing	Ensures everyone has the latest code
Avoid unnecessary edits to analytics.html	Reduces merge conflicts

Rule	Reason
Each person should mainly work in their own JavaScript file	Keeps work separated and easier to merge
Only edit shared files when needed	Prevents overwriting another person's work

Work Areas Confirmed

Person File/Area They Should Mainly Work In

Person 2 adminControls/analytics.html, analytics.css, analytics.js

Person 3 adminControls/sales-report.js

Person 4 adminControls/peak-hours-report.js

Person 5 adminControls/custom-view.js

Person 6 adminControls/export-reports.js

The shared project guide confirms that the team should work inside the adminControls/ area, with each person using their own JavaScript file where possible.

Blockers / Risks Discussed

Blocker or Risk	Solution
Merge conflicts from everyone using the same branch	Always pull the latest branch before working
Multiple people editing analytics.html	Only Person 2 should mainly control the HTML layout
Someone working on outdated code	Pull before making changes and before pushing
CSS or script links missing from the HTML	Communicate before changing shared layout files
Reports not connecting correctly to Person 1's data	Use the confirmed /api/analytics endpoint


Meeting Outcome

By the end of the meeting, the team agreed that Person 1's analytics backend work was complete and ready for the rest of the team to use. The team also agreed to continue working on Person 2's analytics dashboard branch, but with the important rule that everyone must always pull the latest version before making changes or pushing their own code.

This meeting helped the team reduce confusion around branch usage and made it clear how everyone should connect their own Sprint 4 feature to the shared analytics dashboard.

Next Steps

1. Everyone must pull the latest version of Person 2's branch before continuing.
2. Person 2 will keep the main analytics dashboard layout updated.
3. Persons 3, 4, 5, and 6 will work mainly in their own JavaScript files.
4. Everyone will connect their feature to Person 1's completed analytics data.
5. The team will communicate before editing shared files like analytics.html.

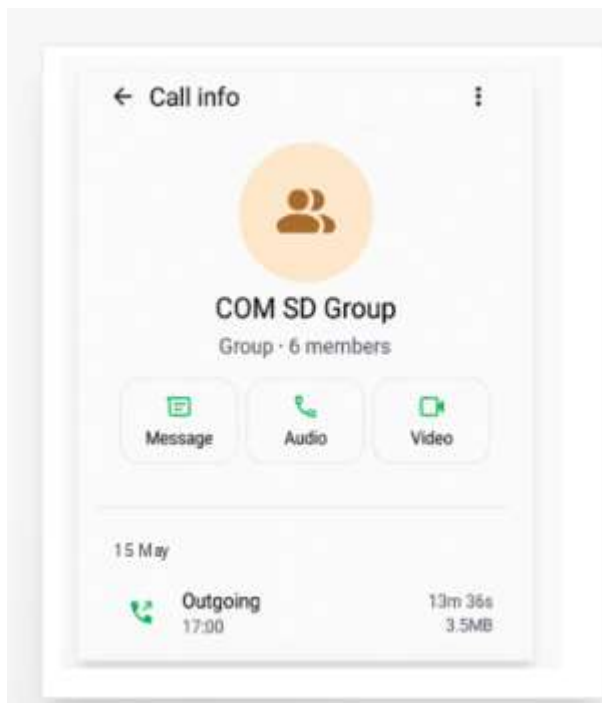

Sprint 4 Daily Scrum Meeting

Date: 17 May 2026

Duration: 10 minutes

Meeting Type: Daily Scrum Meeting

Sprint: Sprint 4

Meeting Summary

The team held a daily scrum meeting to discuss the current progress of Sprint 4 and prepare for the final sprint submission. The team confirmed that almost all parts of Sprint 4 have been completed and that the project is nearly ready for the final sprint review.

Progress Discussed

All main Sprint 4 tasks have been completed by the team. The remaining work is mainly focused on final documentation, exports, diagrams, and the final presentation video.

Sthembile is still working on exporting the PDF documents. This task still needs to be completed by this morning so that the final report and submission files can be prepared properly.

The team was also reminded to send and update their UML diagrams, as these are needed for the final documentation and sprint evidence.

Final Submission Preparation

The team discussed the final sprint video. It was agreed that Sthembile will be responsible for creating the video. Raquel will be responsible for implementing and finalising the final report.

The team is now almost ready for the final sprint, with only a few final items left to complete before submission.

Action Items

Team Member Task


Sthembile	Finish exporting the PDF documents by this morning
Sthembile	Create the final sprint video
Raquel	Implement and finalise the final report
All members	Send or update their UML diagrams

Team Member Task

All members Make sure their Sprint 4 work is complete and ready for submission

Overall Outcome

The meeting confirmed that Sprint 4 is almost complete. The remaining focus is on final polishing, completing the PDF exports, collecting UML diagrams, preparing the video, and finalising the report. The team is nearly ready for the final sprint submission.

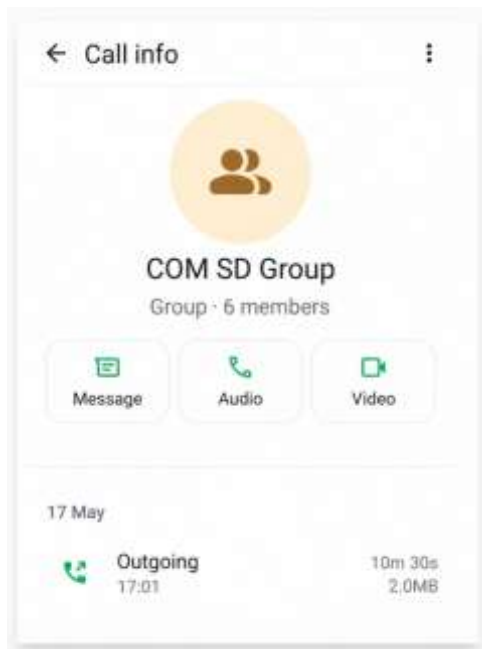

Sprint 4 Sprint Review Meeting

Project: Campus Food Ordering Platform

Sprint: Sprint 4

Meeting Type: Sprint Review Meeting

Date: 18 May 2026

Duration: 15 minutes

Members Present: All Sprint 4 team members

Purpose of the Meeting

The purpose of this Sprint Review Meeting was to review the work completed during Sprint 4, confirm whether the sprint goal was achieved, discuss what went well, identify any challenges, and agree on the final tasks required before submission.

Sprint Review Summary

During the Sprint 4 Review Meeting, the team reviewed the completed work for the admin analytics section of the Campus Food Ordering Platform. The main goal of Sprint 4 was to complete the analytics functionality, including the analytics dashboard, sales per vendor report, peak ordering hours report, custom analytics view, and export functionality.

The team agreed that the Sprint 4 goal was successfully achieved. The analytics features were completed, integrated, and prepared for final testing and submission. The admin analytics page now provides useful reporting features for the admin role and improves the overall completeness of the system.

The team also discussed what went well during the sprint. The task split was clear, each analytics section was completed successfully, and the project is now close to final submission. The dashboard and reports worked well once they were connected to the analytics data.

Some challenges were also identified. The main issue was final integration and ensuring that all analytics sections worked together smoothly. The export feature required extra attention because it needed to work correctly with different reports and filtered data. The team also agreed that communication could still improve, especially by giving more regular progress updates in the group chat instead of waiting until meetings.

GitHub collaboration and merging were also reviewed. The main branch remained stable, and any minor integration issues were fixed. The team agreed that, before adding new code,

members should always pull the latest version of the project and work from updated branches to avoid merge conflicts.

The team confirmed that the UML diagrams were updated, the documentation was being finalised, and the final video and report were discussed. Raquel will complete the final report, while Sthembile will work on the project video.

Final Action Items

Before final submission, the team still needs to:

- Complete final testing of the full system.
- Check that all analytics reports display correctly.
- Confirm that the export functionality works properly.
- Finalise the Sprint 4 evidence and documentation.
- Include the updated UML diagrams.
- Complete the final report.
- Complete the final video.

Closing Statement

Overall, the Sprint 4 Review showed that the sprint was successful. The admin analytics features were completed and integrated, and the project is almost ready for final submission. The remaining focus is on final polishing, testing, documentation, evidence collection, and preparing the final project video.

← Call info



COM SD Group

Group · 6 members



Message



Audio



Video

18 May



Outgoing
10:00

15m 13s
2.3 MB
