

Sprint Burndown Evidence Report

Campus Food Ordering Platform

Software Design Project 2026

Purpose of this evidence document

This PDF collects the sprint burndown evidence for Sprints 1 to 4. Each sprint section includes the exported chart evidence supplied, a short interpretation of the trend, and the supporting CSV data table used for the sprint progress view.

Prepared for submission as sprint burndown chart evidence.

1. Requirement Reference

The sprint burndown requirement expects evidence that shows the progress of work during each sprint. The graphs should show remaining effort over time and should ideally show a downward trend as work is completed.

- **Sprint Burndown Charts:** Graphs showing the progress of work during each sprint. These charts should display the remaining effort over time, ideally showing a downward trend as work is completed.

Requirement excerpt supplied with the evidence: sprint burndown charts must show progress over time.

How to read the charts in this report

The time-series charts show Open items and Completed items across sprint dates. When new tasks are added during backlog refinement, the Open count can temporarily increase. The important evidence is that work is tracked over time and that the Completed count increases as the sprint progresses.

2. Overall Sprint Summary

Sprint	Date range	Start Open	Start Done	Final Open	Final Done	Final completion
Sprint 1	Apr 22 to May 22	16	0	17	15	46.9%
Sprint 2	May 8 to May 22	16	1	14	14	50.0%
Sprint 3	Apr 22 to May 22	0	0	5	9	64.3%
Sprint 4	Apr 22 to May 22	0	0	0	6	100.0%

The summary table above combines the CSV progress evidence with the final board-status snapshots. For Sprint 3, the corrected final board snapshot shows 5 Backlog/Open items and 9 Done items, so Sprint 3 is reported as 64.3% complete instead of 100.0%. Sprint 4 remains correctly closed with 0 open items and 6 completed items.

3. Sprint 1 Burndown Evidence

Sprint focus: Initial project backlog work and early implementation progress.

The CSV evidence for Sprint 1 covers **Apr 22 to May 22**. The sprint started with **16** open item(s) and **0** completed item(s). By the final recorded date, the sprint had **17** open item(s) and **15** completed item(s). The peak open-work count during the recorded period was **22** item(s).

Metric	Value	Meaning for burndown evidence
Date range	Apr 22 to May 22	Shows the sprint tracking period covered by the export.
Completed items added	15	Shows how much work moved into Done during the sprint period.
Final open items	17	Shows remaining work at the final captured date.
Final completed items	15	Shows completed work at the final captured date.
Final completion rate	46.9%	Completed items divided by final Open + Completed count.

Interpretation

Sprint 1 shows early project growth: open work increased as the backlog was refined, while completed work rose to 15 items by the end of the period. This shows both scope discovery and measurable delivery progress.

Sprint 1 - Chart Evidence

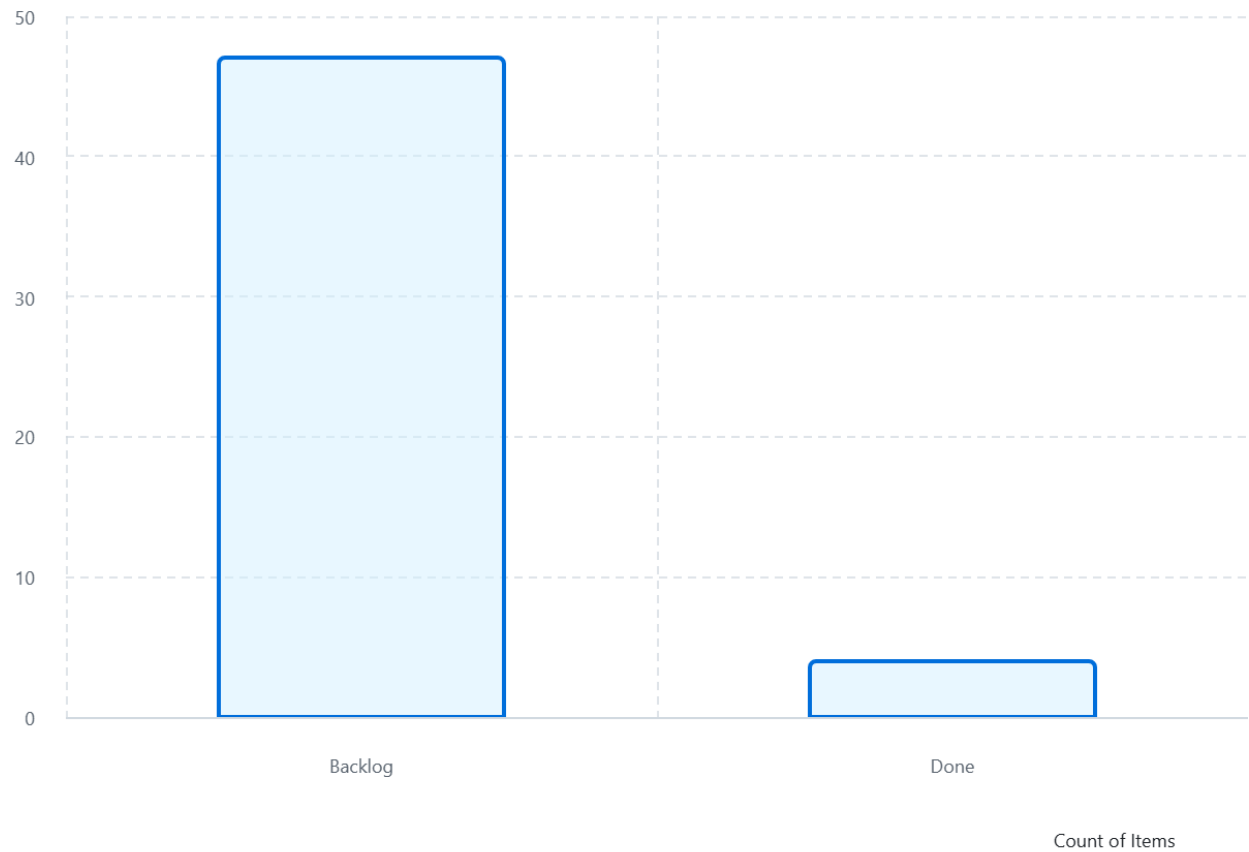


Figure 1.1: Status distribution snapshot for Sprint 1.

This status distribution chart provides a snapshot of the sprint board categories from the exported project report. It is included as supporting evidence that the sprint items were tracked by status.

Sprint 1 - Chart Evidence

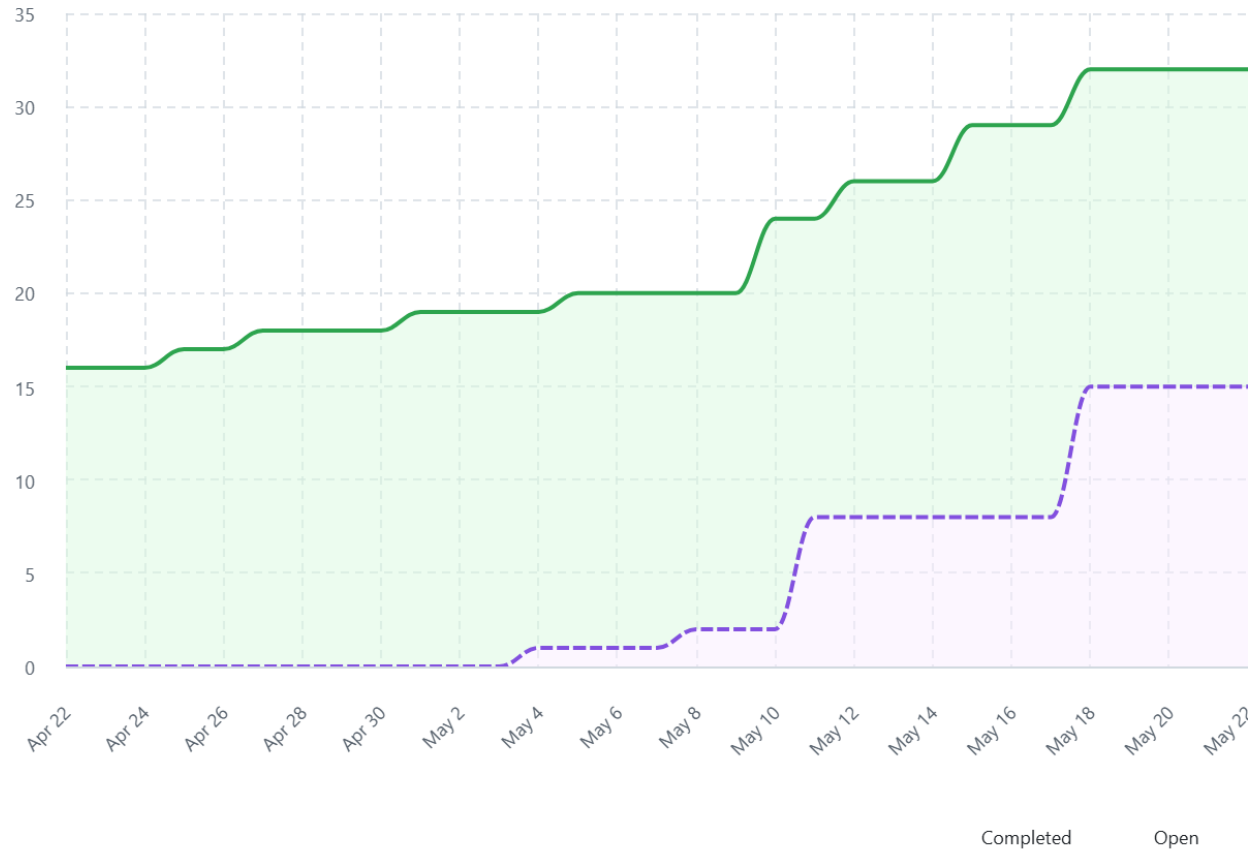


Figure 1.2: Open vs completed items over time for Sprint 1.

This time-series chart is the main burndown-style evidence. It records how Open and Completed items changed over the sprint tracking period.

Sprint 1 - Supporting CSV Data Table

The table below is the supporting data export supplied for this sprint. It records the count of Open and Completed items for each captured date.

Date	Open	Completed
Apr 22	16	0
Apr 23	16	0
Apr 24	16	0
Apr 25	17	0
Apr 26	17	0
Apr 27	18	0
Apr 28	18	0
Apr 29	18	0
Apr 30	18	0
May 1	19	0
May 2	19	0
May 3	19	0
May 4	18	1
May 5	19	1
May 6	19	1
May 7	19	1
May 8	18	2
May 9	18	2
May 10	22	2
May 11	16	8
May 12	18	8
May 13	18	8
May 14	18	8
May 15	21	8
May 16	21	8
May 17	21	8
May 18	17	15
May 19	17	15
May 20	17	15
May 21	17	15
May 22	17	15

4. Sprint 2 Burndown Evidence

Sprint focus: Continued implementation and completion of a larger portion of planned work.

The CSV evidence for Sprint 2 covers **May 8 to May 22**. The sprint started with **16** open item(s) and **1** completed item(s). By the final recorded date, the sprint had **14** open item(s) and **14** completed item(s). The peak open-work count during the recorded period was **20** item(s).

Metric	Value	Meaning for burndown evidence
Date range	May 8 to May 22	Shows the sprint tracking period covered by the export.
Completed items added	13	Shows how much work moved into Done during the sprint period.
Final open items	14	Shows remaining work at the final captured date.
Final completed items	14	Shows completed work at the final captured date.
Final completion rate	50.0%	Completed items divided by final Open + Completed count.

Interpretation

Sprint 2 shows stronger completion progress. The completed line rises from 1 to 14 items, and open work drops from its highest point to 14 by the final date.

Sprint 2 - Chart Evidence

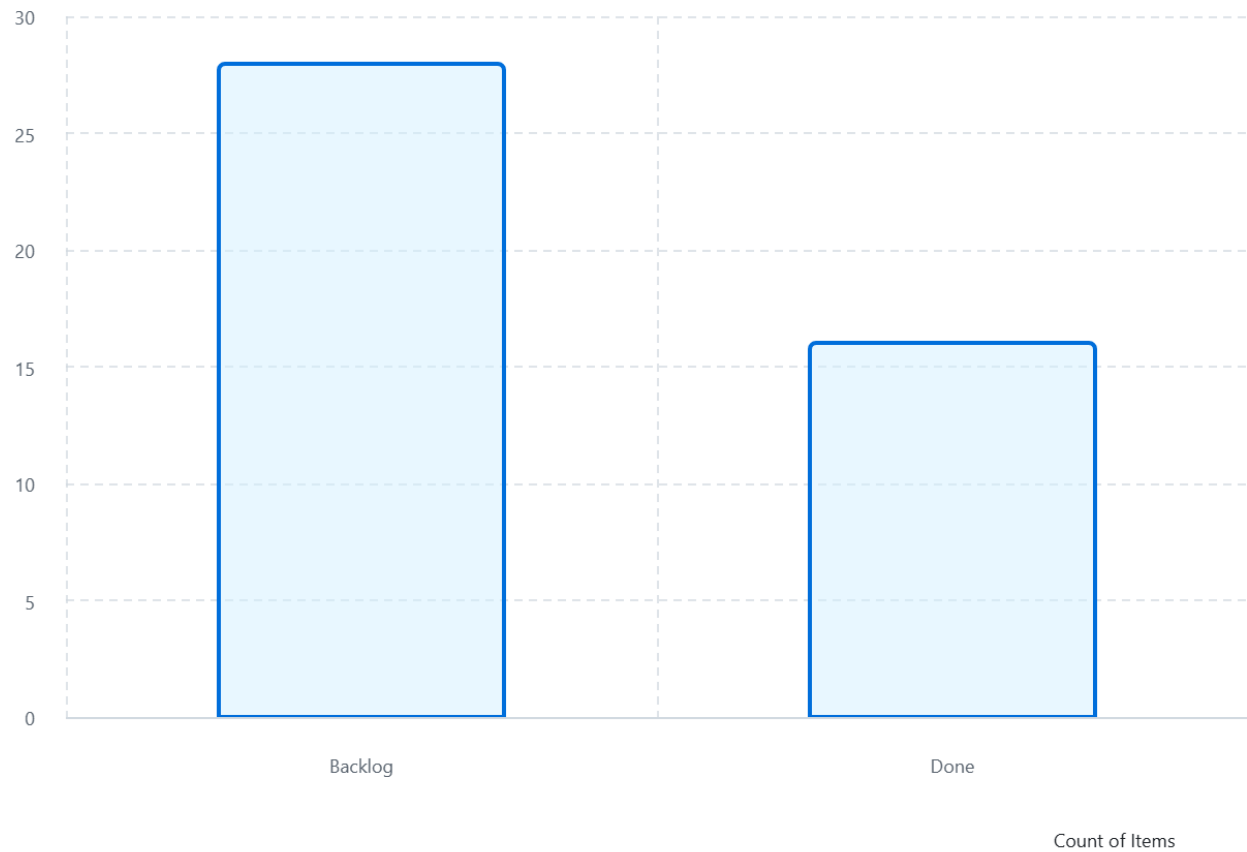


Figure 2.1: Status distribution snapshot for Sprint 2.

This status distribution chart provides a snapshot of the sprint board categories from the exported project report. It is included as supporting evidence that the sprint items were tracked by status.

Sprint 2 - Chart Evidence

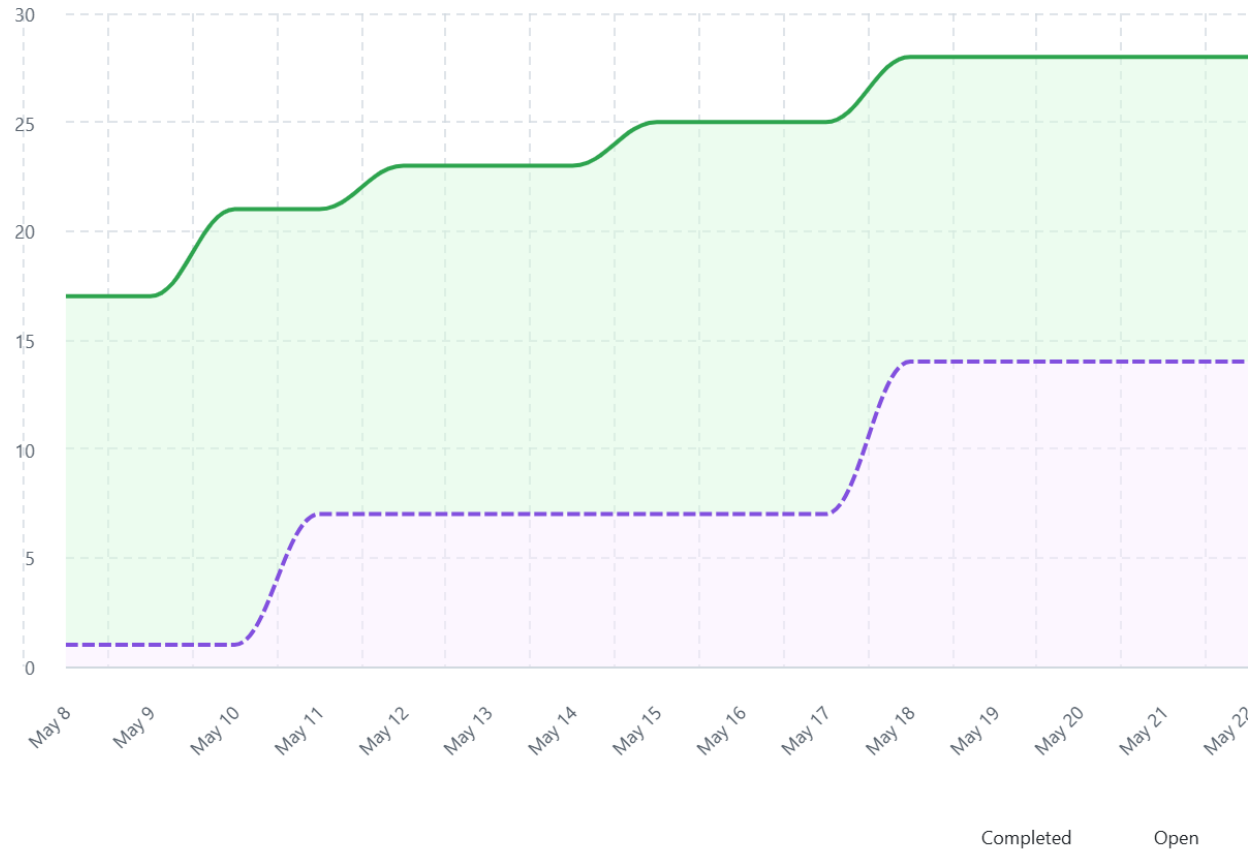


Figure 2.2: Open vs completed items over time for Sprint 2.

This time-series chart is the main burndown-style evidence. It records how Open and Completed items changed over the sprint tracking period.

Sprint 2 - Supporting CSV Data Table

The table below is the supporting data export supplied for this sprint. It records the count of Open and Completed items for each captured date.

Date	Open	Completed
May 8	16	1
May 9	16	1
May 10	20	1
May 11	14	7
May 12	16	7
May 13	16	7
May 14	16	7
May 15	18	7
May 16	18	7
May 17	18	7
May 18	14	14
May 19	14	14
May 20	14	14
May 21	14	14
May 22	14	14

5. Sprint 3 Burndown Evidence

Sprint focus: Online payments and dietary system work, including tracked progress to completed items.

The corrected Sprint 3 evidence is read using both the time-series chart and the board-status snapshot. The CSV progress chart shows completed work increasing during the sprint, but the updated board-status chart shows 5 remaining Backlog/Open item(s) and 9 Done item(s). Therefore Sprint 3 is not treated as 0 open or 100.0% complete in the final summary.

Metric	Value	Meaning for burndown evidence
Date range	Apr 22 to May 22	Shows the sprint tracking period covered by the evidence.
Completed / Done items	9	Shows work in Done in the final board snapshot.
Final open / backlog items	5	Shows remaining Backlog/Open work in the final board snapshot.
Final completed / done items	9	Shows completed work in the final board snapshot.
Final completion rate	64.3%	Done items divided by final Backlog + Done count: $9/(5+9)$.

Interpretation

Sprint 3 shows measurable progress, but it should not be reported as fully closed. The corrected board-status snapshot shows 9 completed items and 5 items still in Backlog/Open, giving a final completion rate of 64.3%. This now follows the same logic used for Sprint 1 and Sprint 2, where final open work represents remaining items and final completed work represents items moved to Done.

Sprint 3 - Chart Evidence

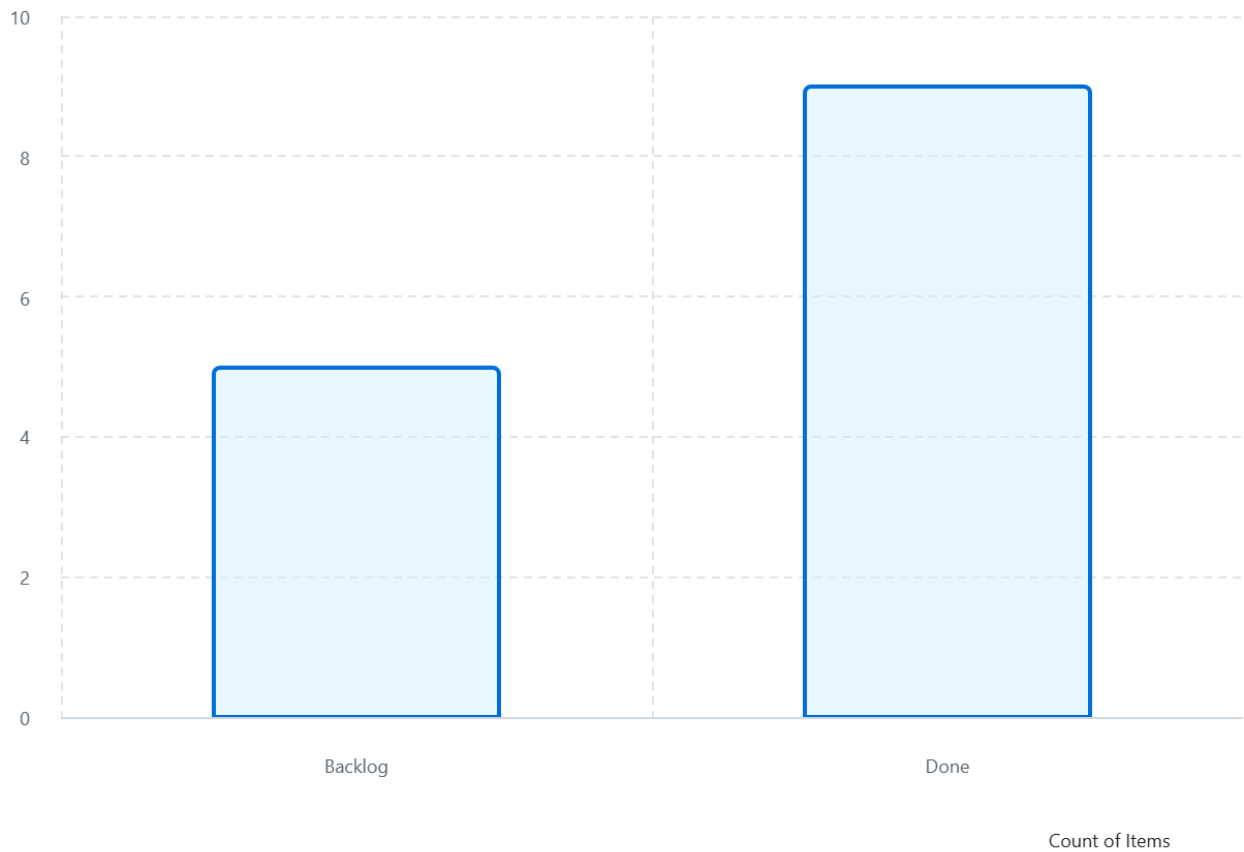


Figure 3.1: Status distribution snapshot for Sprint 3.

This status distribution chart provides a snapshot of the sprint board categories from the exported project report. It is included as supporting evidence that the sprint items were tracked by status.

Sprint 3 - Chart Evidence

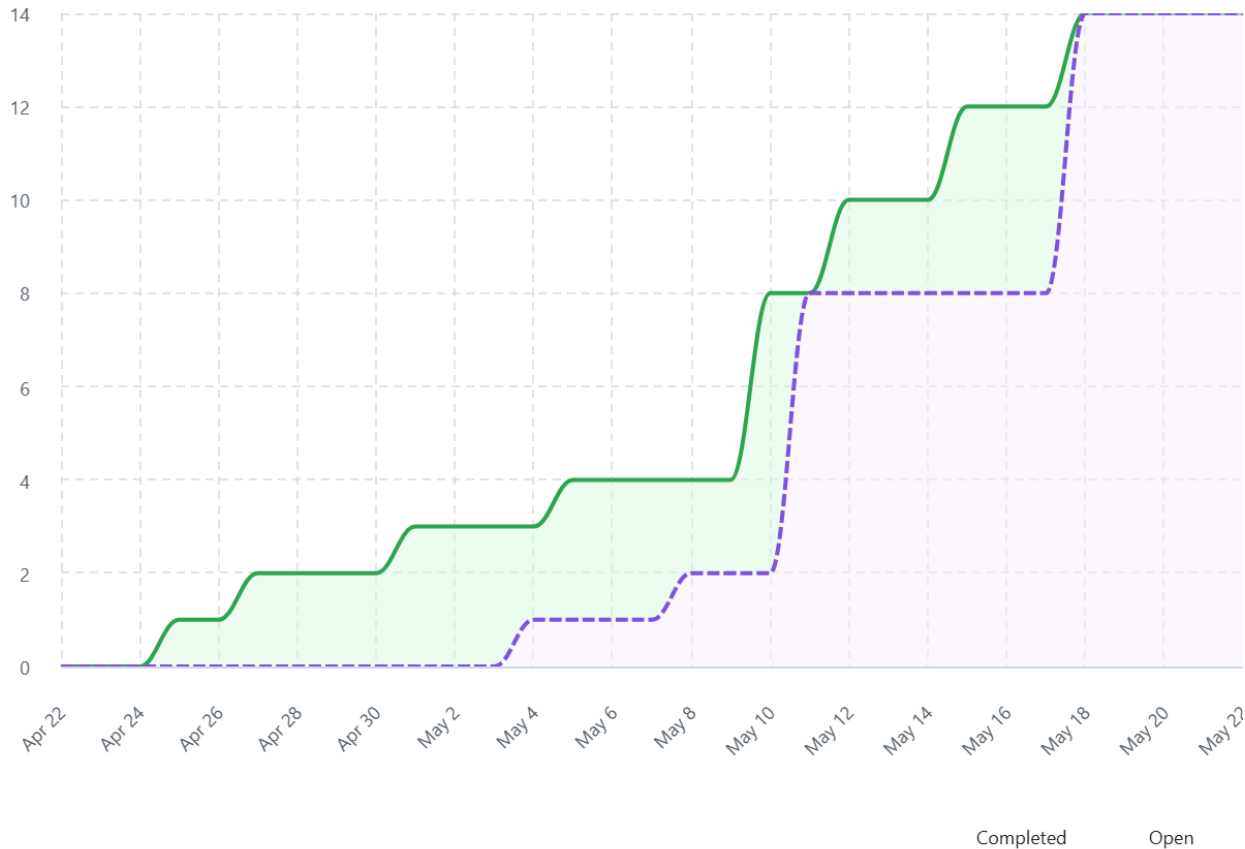


Figure 3.2: Open vs completed items over time for Sprint 3.

This time-series chart is the main burndown-style evidence. It records how Open and Completed items changed over the sprint tracking period.

Sprint 3 - Supporting CSV Data Table

The table below is the supporting data export supplied for this sprint. It records the count of Open and Completed items for each captured date.

Date	Open	Completed
Apr 22	0	0
Apr 23	0	0
Apr 24	0	0
Apr 25	1	0
Apr 26	1	0
Apr 27	2	0
Apr 28	2	0
Apr 29	2	0
Apr 30	2	0
May 1	3	0
May 2	3	0
May 3	3	0
May 4	2	1
May 5	3	1
May 6	3	1
May 7	3	1
May 8	2	2
May 9	2	2
May 10	6	2
May 11	0	8
May 12	2	8
May 13	2	8
May 14	2	8
May 15	4	8
May 16	4	8
May 17	4	8
May 18	0	14
May 19	0	14
May 20	0	14
May 21	0	14
May 22	0	14

Sprint 3 correction note

Correction note: this page keeps the raw time-series CSV export. The final Sprint 3 summary uses the updated board-status snapshot: 5 Backlog/Open items and 9 Done items, so Sprint 3 is not reported as 0 open or 100.0% complete.

6. Sprint 4 Burndown Evidence

Sprint focus: Analytics work and final completion evidence.

The CSV evidence for Sprint 4 covers **Apr 22 to May 22**. The sprint started with **0** open item(s) and **0** completed item(s). By the final recorded date, the sprint had **0** open item(s) and **6** completed item(s). The peak open-work count during the recorded period was **4** item(s).

Metric	Value	Meaning for burndown evidence
Date range	Apr 22 to May 22	Shows the sprint tracking period covered by the export.
Completed items added	6	Shows how much work moved into Done during the sprint period.
Final open items	0	Shows remaining work at the final captured date.
Final completed items	6	Shows completed work at the final captured date.
Final completion rate	100.0%	Completed items divided by final Open + Completed count.

Interpretation

Sprint 4 shows final sprint closure. The tracked analytics work starts appearing during May, then all 6 tracked items move to completed with 0 open items remaining by the final captured dates.

Sprint 4 - Chart Evidence




Figure 4.1: Status distribution snapshot for Sprint 4.

This status distribution chart provides a snapshot of the sprint board categories from the exported project report. It is included as supporting evidence that the sprint items were tracked by status.

Sprint 4 - Chart Evidence

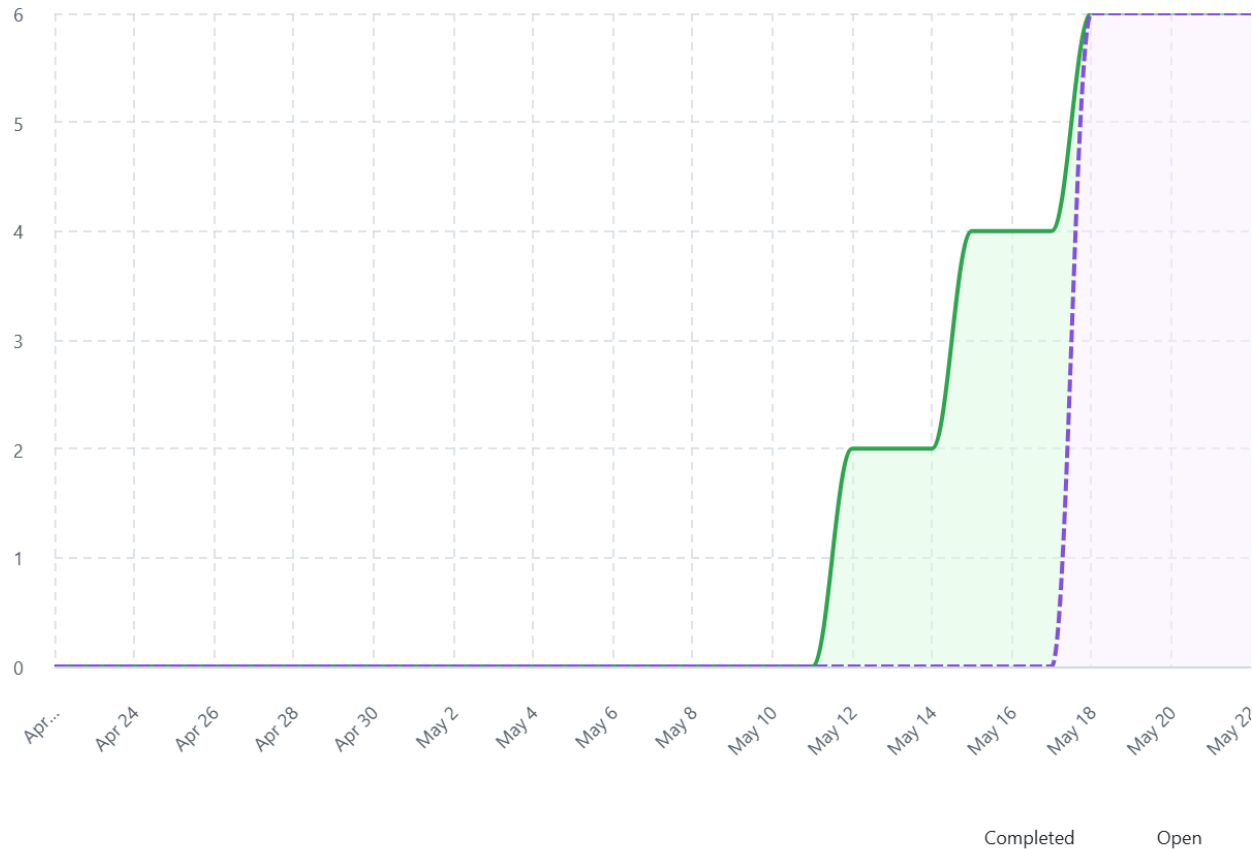


Figure 4.2: Open vs completed items over time for Sprint 4.

This time-series chart is the main burndown-style evidence. It records how Open and Completed items changed over the sprint tracking period.

Sprint 4 - Supporting CSV Data Table

The table below is the supporting data export supplied for this sprint. It records the count of Open and Completed items for each captured date.

Date	Open	Completed
Apr 22	0	0
Apr 23	0	0
Apr 24	0	0
Apr 25	0	0
Apr 26	0	0
Apr 27	0	0
Apr 28	0	0
Apr 29	0	0
Apr 30	0	0
May 1	0	0
May 2	0	0
May 3	0	0
May 4	0	0
May 5	0	0
May 6	0	0
May 7	0	0
May 8	0	0
May 9	0	0
May 10	0	0
May 11	0	0
May 12	2	0
May 13	2	0
May 14	2	0
May 15	4	0
May 16	4	0
May 17	4	0
May 18	0	6
May 19	0	6
May 20	0	6
May 21	0	6
May 22	0	6

Final Submission Note

This report includes all supplied sprint graph evidence and the matching CSV tables for Sprints 1 to 4. The report can be submitted as evidence that sprint progress was tracked using burndown-style charts and supporting data exports.

Evidence included

Sprint 1: status chart, open/completed time-series chart, CSV table. Sprint 2: status chart, open/completed time-series chart, CSV table.
Sprint 3: status chart, open/completed time-series chart, CSV table. Sprint 4: status chart, open/completed time-series chart, CSV table.
