

Daily Stand-Up and Sprint Retrospective Evidence

Campus Food Ordering Platform

Combined Scrum Evidence Document

Project	Campus Food Ordering Platform
Evidence Type	Daily stand-up / Scrum meeting evidence and sprint retrospective evidence
Purpose	To show team communication, progress tracking, blockers, outcomes, and sprint reflection across Sprints 1 to 4.
Source Documents	Daily_Standup_Evidence.docx and Sprint_Retrospective_Evidence.docx
Structure	Each sprint contains daily/Scrum meeting evidence first, followed by the sprint retrospective evidence.

Evidence order: Sprint daily meetings → Sprint retrospective meeting → next sprint

1. Evidence Overview

This combined document brings together the daily stand-up/Scrum meeting evidence and the retrospective evidence into one clean file. The retrospective meeting for each sprint is placed directly after that sprint's daily/Scrum meetings.

Sprint	Daily / Scrum Evidence	Retrospective Evidence	Main Focus
Sprint 1	Planning, Scrum check-in, progress, review preparation	13 April 2026 retrospective	Authentication, roles, menu management, admin controls
Sprint 2	Planning, daily scrum, final progress	20 April 2026 retrospective	Cart, orders, vendor dashboard, tracking, notifications
Sprint 3	Planning, progress meetings, merge/review preparation	11 May 2026 retrospective	PayFast payments, dietary system, one-vendor rule
Sprint 4	Planning, branch coordination, final preparation/review	18 May 2026 retrospective	Analytics, exports, UML diagrams, final submission

2. Sprint 1 Evidence

Sprint 1 focused on building the platform foundation, including authentication, role-based access, menu management, admin controls, and early GitHub workflow setup.

Supporting daily/Scrum evidence file: Sprint1.docx

Sprint 1 Daily / Scrum Meetings

Meeting	Date / Duration	Purpose	Evidence
Planning Meeting	30 March 2026 1 hour 30 minutes	Sprint planning, task breakdown, user story discussion, and initial project structure.	Sprint1.docx
Scrum / Planning Meeting	7 April 2026 16 minutes	CI/CD discussion, GitHub Issues, acceptance tests, vendor approval, and branching strategy.	Sprint1.docx
Progress Meeting	10 April 2026 30 minutes	Progress check, completed login/registration functionality, admin access decision, and vendor dashboard planning.	Sprint1.docx

Main discussion summary

- The team agreed that Sprint 1 would focus on user verification and menu management.
- User stories were identified for student, vendor, and admin roles.
- The team discussed role-based access, vendor approval, menu creation, and GitHub project tracking.
- The CI/CD pipeline and branch workflow were discussed, but the team was still learning how to apply the workflow properly.

Blockers / risks discussed

- Task splitting was not fully clear at the beginning of the sprint.
- Some members were still unsure how their work connected to the full system.
- Presentation preparation happened late.
- The team needed stronger GitHub workflow discipline.

Outcomes / next steps


- Sprint 1 focus areas and user stories were agreed.
- Development began after planning.
- Authentication-related functionality was reviewed and confirmed.
- The team identified improvements for Sprint 2, especially task ownership and GitHub workflow.

Daily / Scrum screenshot evidence


Supporting Evidence

A detailed Sprint 1 guide/document was created to summarise all decisions, responsibilities, system design, and technical approach discussed in the meeting.

(Posting this for record purposes as this was the first team meeting.)

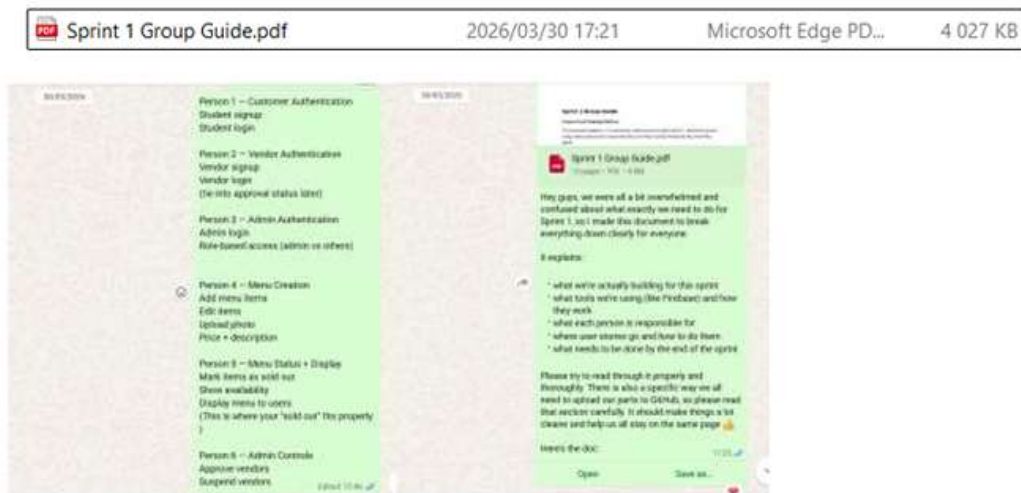

Sprint 1 planning/group guide evidence.

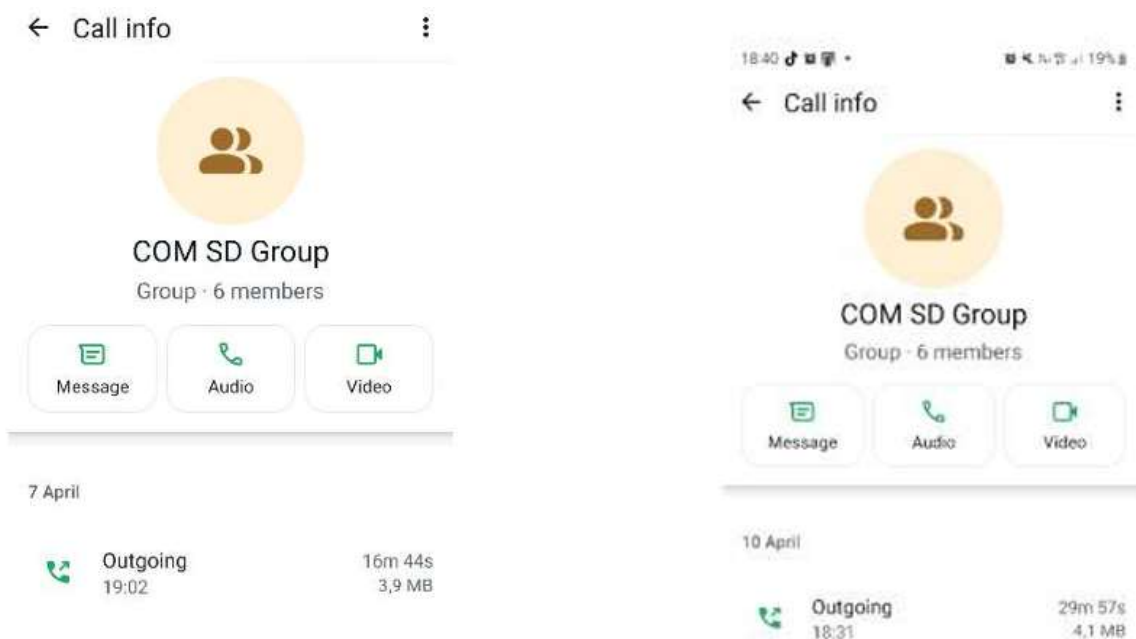

Sprint 1 Scrum / Planning Meeting - 7 April.

Sprint 1 Progress Meeting - 10 April.

Sprint 1 Retrospective Meeting Evidence

Field	Details
Date	13 April 2026
Platform	WhatsApp Call
Duration	Approx. 19 minutes
Attendees	All team members
Purpose	Reflect on the first sprint and identify improvements for task splitting, GitHub workflow, and communication.
Sprint focus	User verification, menu management, role-based access, admin vendor controls, GitHub workflow setup.

Retrospective Area	Summary
What went well	Core foundation features were completed. There were no major technical blockers. The team had enough working functionality to present.
What could be improved	Tasks were not split clearly or fairly. Some members carried more work than others. GitHub was difficult to manage and the branch workflow was not followed consistently.
Challenges / blockers	Unclear task ownership, uneven workload distribution, and weak GitHub workflow control.
Action items	Break user stories into smaller tasks, assign owners clearly, use GitHub Issues and Projects properly, use feature branches and pull requests, and hold more frequent check-ins.



Retrospective evidence screenshot - Sprint 1.

Evidence conclusion: The retrospective confirmed that Sprint 1 achieved the basic functionality but showed that team organisation and GitHub workflow needed improvement.

3. Sprint 2 Evidence

Sprint 2 focused on the ordering workflow, including cart functionality, order placement, vendor order management, student tracking, and notifications.

Supporting daily/Scrum evidence file: Sprint 2.docx

Sprint 2 Daily / Scrum Meetings

Meeting	Date / Duration	Purpose	Evidence
Sprint Planning Meeting	15 April 2026 Approx. 27 minutes	Backlog selection, task allocation, workflow agreements, and improved task ownership.	Sprint 2.docx
Daily Scrum Meeting	17 April 2026 Approx. 16 minutes	Progress updates, alignment check, GitHub branch reminders, and pull request workflow.	Sprint 2.docx
Daily Scrum / Final Progress Meeting	19 April 2026 Approx. 29 minutes	End-to-end system progress review, final fixes, notifications, and timestamp display discussion.	Sprint 2.docx

Main discussion summary

- Sprint 2 tasks were split more clearly than Sprint 1.
- The team focused on cart, orders, backend logic, vendor dashboards, status updates, and student tracking.
- Daily Scrum meetings confirmed steady progress and no major blockers.
- Final progress checks identified only small issues such as notifications and timestamp display.


Blockers / risks discussed

- No major blockers were reported during the daily Scrum meetings.
- Minor remaining work included notification completion and timestamp display fixes.

Outcomes / next steps

- Sprint 2 work was confirmed to be on track.
- The team used branches and pull requests more consistently.
- The ordering workflow was nearly complete by the final progress meeting.


Daily / Scrum screenshot evidence

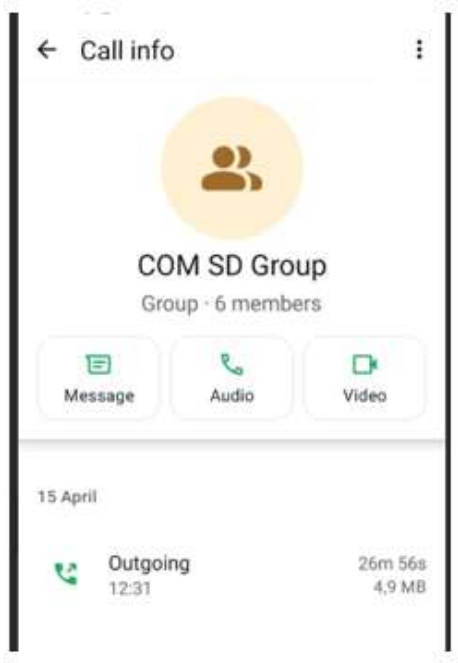

Sprint 2 Planning Meeting - 15 April.



Sprint 2 Daily Scrum Meeting - 17 April.

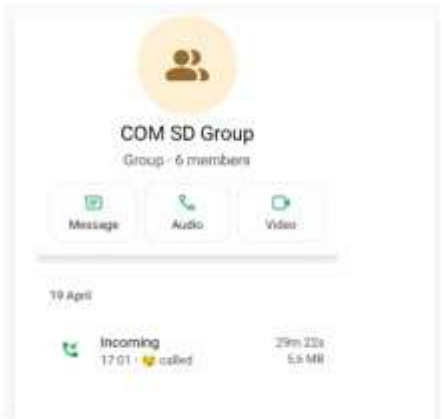


Sprint 2 Final Progress Meeting - 19 April.

Sprint 2 Retrospective Meeting Evidence

Field	Details
Date	20 April 2026
Platform	WhatsApp Call
Duration	11m 32s
Attendees	All team members
Purpose	Reflect on the ordering workflow sprint and improve documentation, dependency planning, and testing workflow.
Sprint focus	Cart functionality, order placement, vendor orders dashboard, order status updates, student tracking, notifications.

Retrospective Area	Summary
What went well	Task distribution improved. Communication through WhatsApp meetings was more effective. Feature branches and pull requests were used. CI/CD worked smoothly and the main tasks were completed on time.
What could be improved	UML and architecture documentation were left too late. Some non-coding requirements were not identified early enough. Codecov and testing tools still needed clarification.
Challenges / blockers	The sprint was short and required careful dependency planning. Documentation and UML preparation needed to start earlier.
Action items	Start UML and documentation earlier, continue prioritising dependency-heavy tasks, maintain the feature-branch workflow, and keep the GitHub Projects board updated.

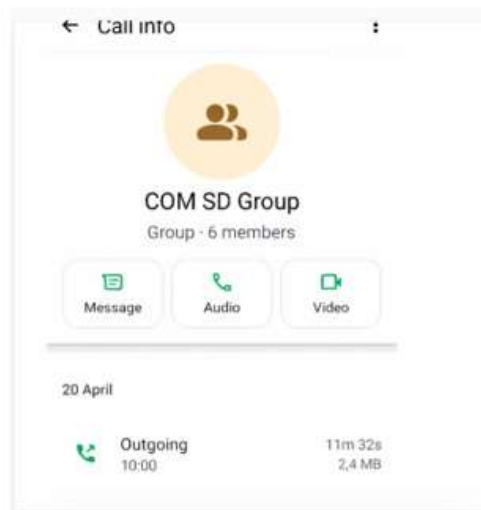

Retrospective evidence screenshot - Sprint 2.

Evidence conclusion: The retrospective showed that Sprint 2 improved strongly compared with Sprint 1, while documentation planning still needed attention.

4. Sprint 3 Evidence

Sprint 3 focused on online payments and the dietary system, including PayFast integration, one-vendor checkout, paid-order handling, active orders, order history, and dietary filtering.

Supporting daily/Scrum evidence file: Sprint 3.docx

Sprint 3 Daily / Scrum Meetings

Meeting	Date / Duration	Purpose	Evidence
Sprint Planning Meeting	24 April 2026 30 minutes	Payment feature planning, dietary system planning, and task dependency order.	Sprint 3.docx
Progress Meeting	30 April 2026 16 minutes	PayFast decision, one-vendor checkout rule, paid orders, active orders, order history, and dietary options.	Sprint 3.docx
Progress Meeting	8 May 2026 15 minutes	Payment progress, student-side progress, vendor-side review, and dietary feature progress.	Sprint 3.docx
Review / Final Progress Meeting	11 May 2026 12-17 minutes	Review of completed payment and dietary features, branch issues, and next sprint actions.	Sprint 3.docx

Main discussion summary

- The team agreed that Sprint 3 would focus on online payments and dietary filtering.
- PayFast was selected for the payment flow.
- The one-vendor cart rule was agreed to simplify payment and order tracking.
- Progress meetings confirmed payment completion and tracked student, vendor, and dietary feature progress.


Blockers / risks discussed

- Some tasks depended on foundational work being completed first.
- Payment and dietary tag formats needed coordination.
- Branch management and outdated code became a risk during integration.


Outcomes / next steps

- Payment and dietary features were completed and integrated.
- The team planned final merging and UML updates.
- The team agreed to improve communication and branch management in Sprint 4.


Daily / Scrum screenshot evidence

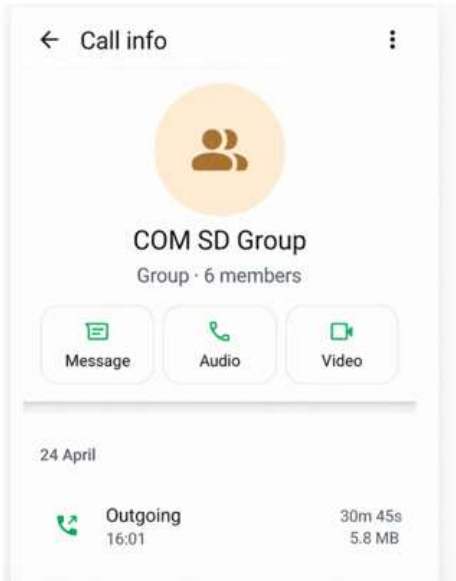


Sprint 3 Planning Meeting - 24 April.

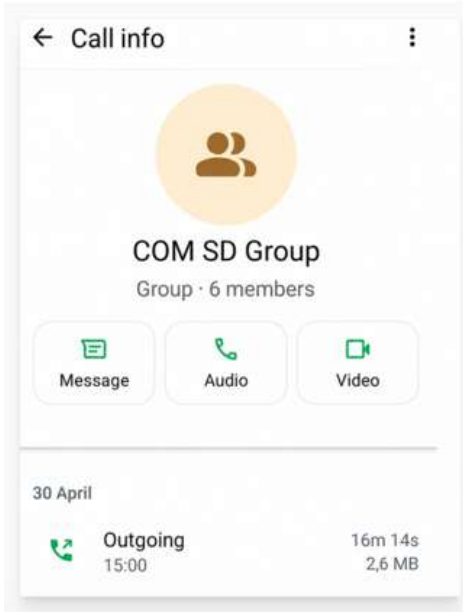

Sprint 3 Progress Meeting - 30 April.



Sprint 3 Progress Meeting - 8 May.

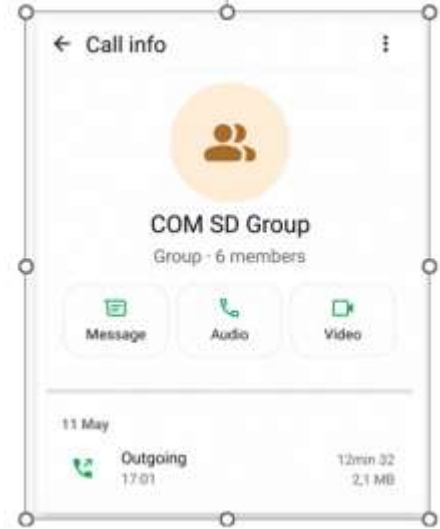


Sprint 3 Review / Final Progress Meeting - 11 May.

Sprint 3 Retrospective Meeting Evidence

Field	Details
Date	11 May 2026
Platform	WhatsApp Call
Duration	17m 35s
Attendees	All team members
Purpose	Review and reflect on payment and dietary system completion before the final sprint.
Sprint focus	PayFast payment API, payment notify endpoint, paid order handling, one-vendor cart rule, active orders, order history, dietary tags and filtering.

Retrospective Area	Summary
What went well	The sprint goal was achieved. Payment and dietary features were completed and integrated. The task split was fair and clear, and the main branch remained stable after final integration.
What could be improved	GitHub branch management still needed improvement. One team member worked from an outdated branch, which made merging more difficult. Progress updates in the group chat were not always consistent.
Challenges / blockers	The main difficulty was GitHub-related, especially outdated branches and merge conflicts. No major technical blocker remained unresolved.
Action items	Pull the latest main branch before working, give more regular progress updates, ask for help earlier, review work before final merges, and update UML diagrams when the system changes.

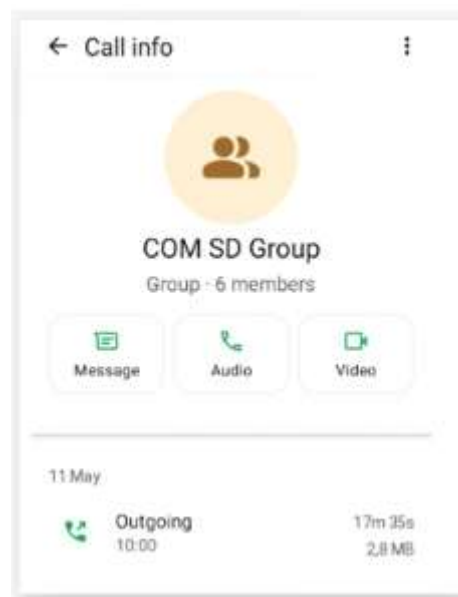

Retrospective evidence screenshot - Sprint 3.

Evidence conclusion: The retrospective confirmed that Sprint 3 was successful but highlighted the need for stricter branch management and better communication.

5. Sprint 4 Evidence

Sprint 4 focused on admin analytics, report exports, testing evidence, UML diagrams, and final submission preparation.

Supporting daily/Scrum evidence file: Sprint 4.docx

Sprint 4 Daily / Scrum Meetings

Meeting	Date / Duration	Purpose	Evidence
Planning and Task Breakdown Meeting	12 May 2026 25 minutes	Analytics goal, task breakdown, team roles, work order, and dependencies.	Sprint 4.docx
Daily Scrum / Branch Coordination Meeting	15 May 2026 13 minutes	Person 1 analytics backend completion, API endpoint discussion, branch coordination, and conflict prevention.	Sprint 4.docx
Sprint Review / Methodology Review Meeting	18 May 2026 15 minutes	Review final Sprint 4 work, Scrum methodology evidence, final artefacts, and submission readiness.	Sprint 4.docx

Main discussion summary

- Sprint 4 focused on the admin analytics section.
- The analytics work was split into backend data, dashboard layout, sales report, peak hours report, custom view, and CSV/PDF export.
- The branch coordination meeting confirmed that members must pull the latest branch before editing or pushing.
- Final meetings focused on evidence, UML diagrams, video preparation, and submission readiness.


Blockers / risks discussed

- Reports depended on clean analytics data.
- Export functionality depended on report data being ready.
- Multiple people editing shared files could cause merge conflicts.
- Final submission evidence needed careful organisation.


Outcomes / next steps

- Sprint 4 analytics goal was agreed and completed.
- Individual responsibilities and dependencies were confirmed.
- The team moved into final polishing, evidence preparation, and submission checking.


Daily / Scrum screenshot evidence

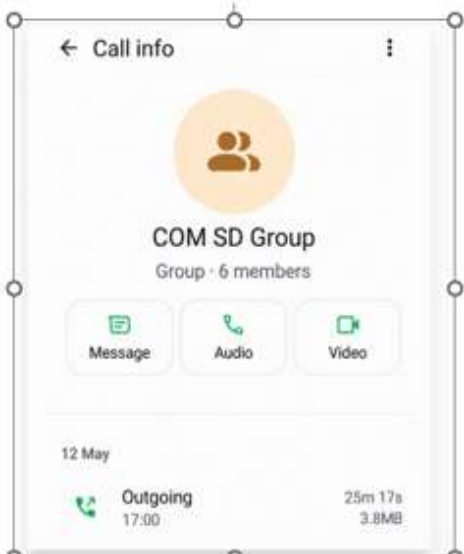

Sprint 4 Planning Meeting - 12 May.



Sprint 4 Branch Coordination Meeting.

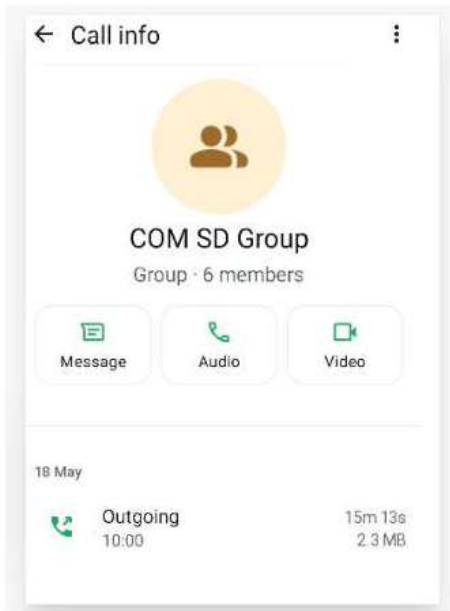


Sprint 4 Review / Methodology Review Meeting - 18 May.

Sprint 4 Retrospective Meeting Evidence

Field	Details
Date	18 May 2026
Platform	WhatsApp Call
Duration	15m 13s
Attendees	All team members
Purpose	Review analytics completion and agree on final documentation, testing evidence, and submission tasks.
Sprint focus	Analytics data foundation, analytics dashboard, sales per vendor report, peak ordering hours report, custom analytics view, CSV/PDF export, final documentation.

Retrospective Area	Summary
What went well	The task breakdown was clear from the start. Analytics features were completed and integrated. Scrum evidence and final artefacts were organised more carefully for final submission.
What could be improved	Final documentation took a lot of time. Evidence, screenshots, and links had to be organised carefully. All public links still needed final checking.
Challenges / blockers	The main challenge was final organisation rather than coding. The team needed to check links, evidence, video, and Moodle submission readiness.
Action items	Check the hosted app, GitHub repository, video, Scrum artefacts, additional artefacts, Codecov evidence, final form, and Moodle submission before the deadline.

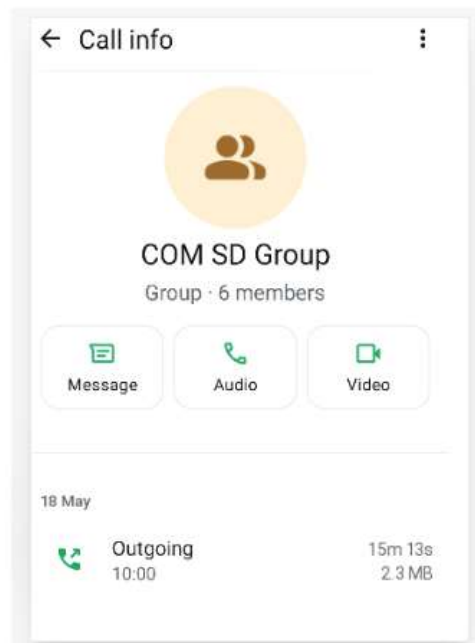

Retrospective evidence screenshot - Sprint 4.

Evidence conclusion: The retrospective confirmed that Sprint 4 was successful and that the remaining work was final submission checking and polishing.

Final Evidence Conclusion

Conclusion: This combined evidence document confirms that the team held Scrum meetings, daily progress check-ins, and sprint retrospectives across Sprints 1 to 4. The evidence shows progress tracking, blocker discussion, task coordination, and continuous improvement throughout the project.
